


**HOPE UNIVERSITY COLLEGE**  
**ADDIS ABABA**  
**ETHIOPIA**

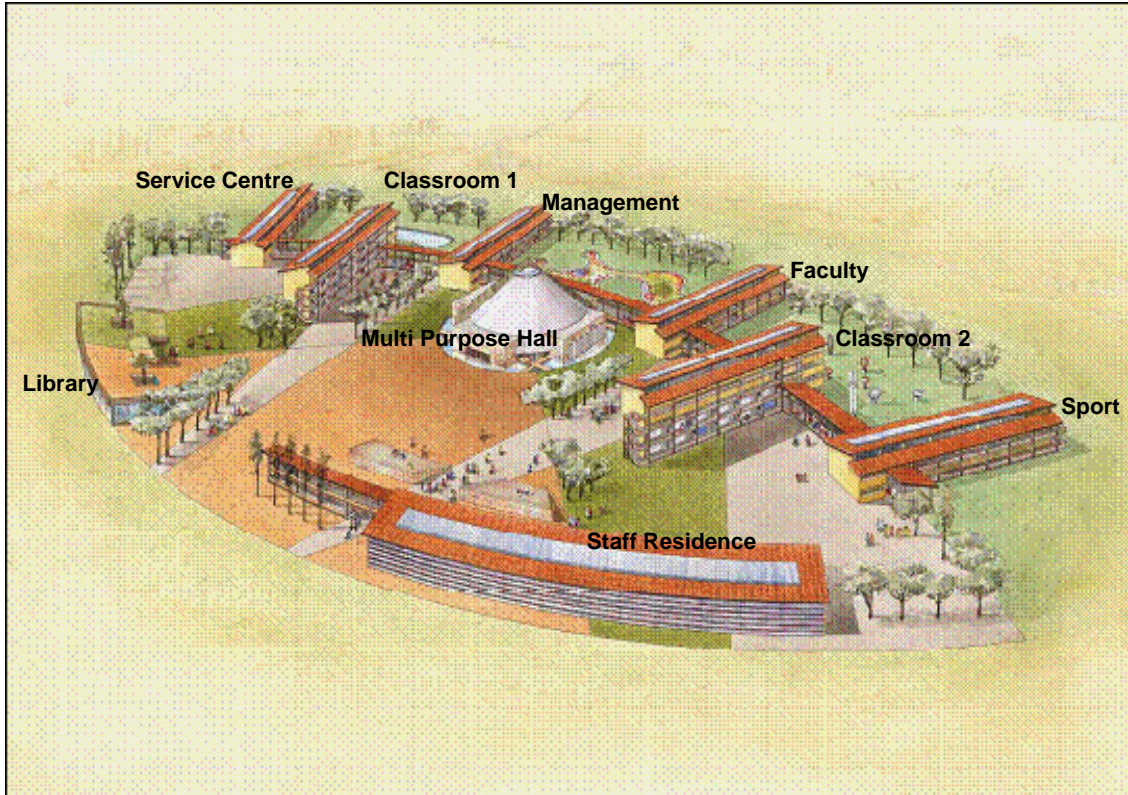

**PROGRESS REPORT**

**Project** : Construction of Hope University College  
**To** : Dr. Minas Hiruy, Building Consortium (Holland), Ethiopiaid  
UK, Menlo Park (USA), Ethiopiaid Ireland  
**Date** : 27 October 2008  
**Prepared by** : Niek Hoffius

---



### **Service Centre**

The corrugated iron roof has been installed (not to be seen on the pictures) and plasterwork to the inside and the outside of the building is in progress.

*Het golfplaten dak is gelegd (niet te zien op de foto's) en het pleisterwerk aan de binnen- en buitenkant van het gebouw is aan de gang.*



### **Classroom Building 1**

Block laying and plasterwork is in progress.

*Metselwerk en pleisterwerk is aan de gang.*



**Administration Building**

The corrugated iron roof has been installed and the laying of blocks is finished, while plasterwork is in progress.

*Het golfplaten dak is gelegd en het metselwerk is gereed, terwijl het pleisterwerk aan de gang is.*



**Faculty Office  
&  
Classroom Building 2**

The concrete structure of the faculty office (at the left) is ready and the fourth and last floor of the second classroom building is under construction.

*Het betonskelet van het faculteitskantoor is gereed en de derde en laatste verdieping van het tweede classroom gebouw is in aanbouw.*



### **Knowledge Centre (Library)**

The sloped roof is under construction, steel fixers are still busy fixing the reinforcing steel. After the concrete roof is finished and made watertight, it will be covered by a 600 millimeter (approximately 2 feet) layer of soil to be sown in with grass.

*Het schuine dak is in aanbouw, vlechters zijn bezig met het vlechten van het betonstaal. Nadat het betondak klaar is en waterdicht gemaakt, zal het bedekt worden met een 600 mm dikke laag grond die ingezaaid zal worden met gras.*



### **Staff Residence Building**

The concrete structure is in progress.

*Het betonskelet is in aanbouw.*
